



# SR 28 CMAR - Project Status

- GMP# 1: Undercrossing, utilities, & parking - **\$4.3M: COMPLETE**
- GMP# 2: Path, WQ, ITS, & Safety - \$36 M
  - Day 201 of 250 Working Days: 80% complete
  - Anticipated completion in the Spring 2019
- IVGID Change Order - \$1.2M
  - 95% Complete

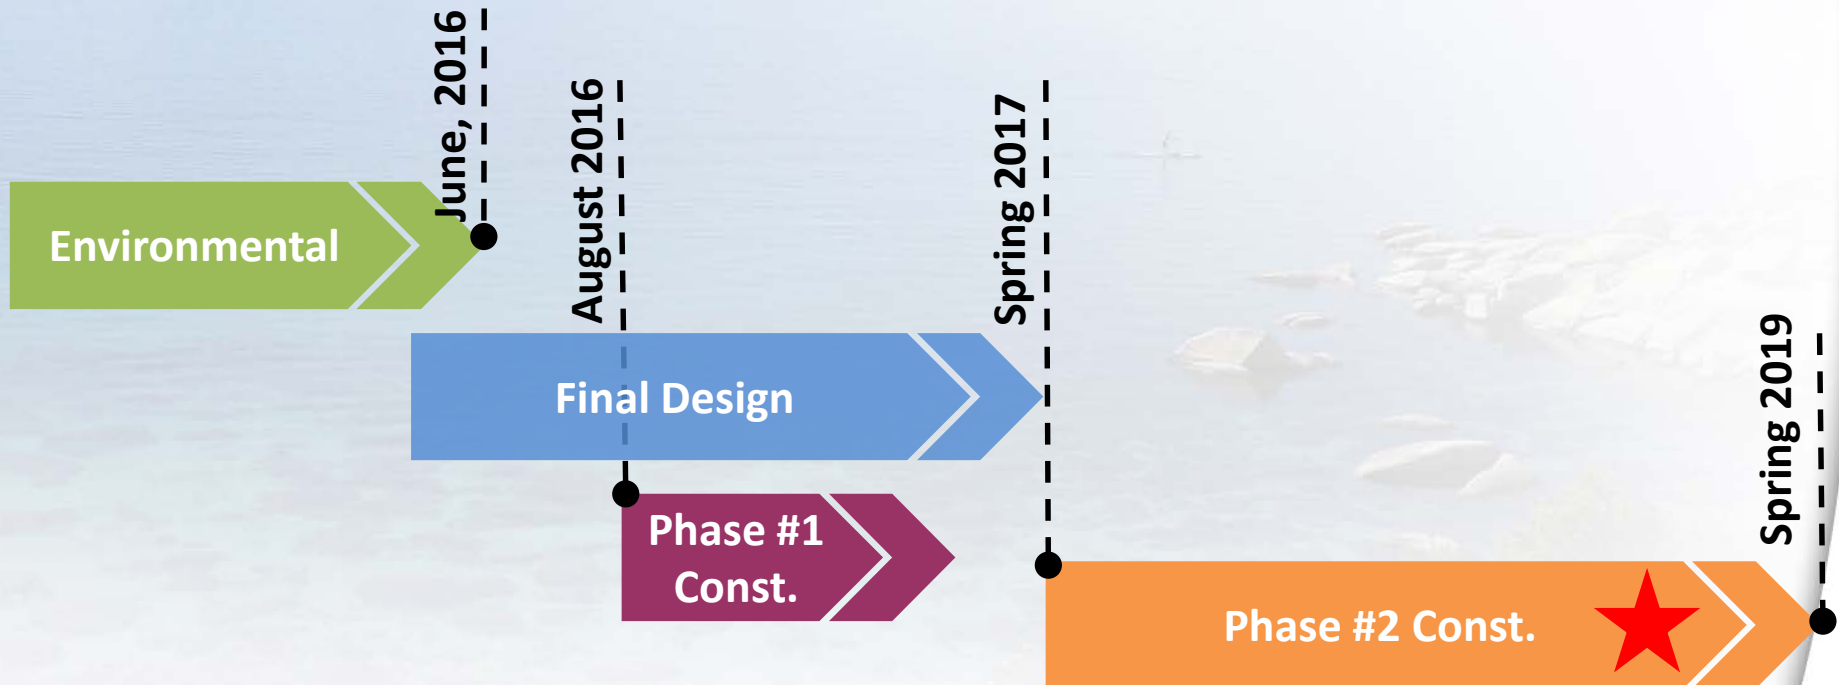

# GMP# 1 Construction – 2016 Construction

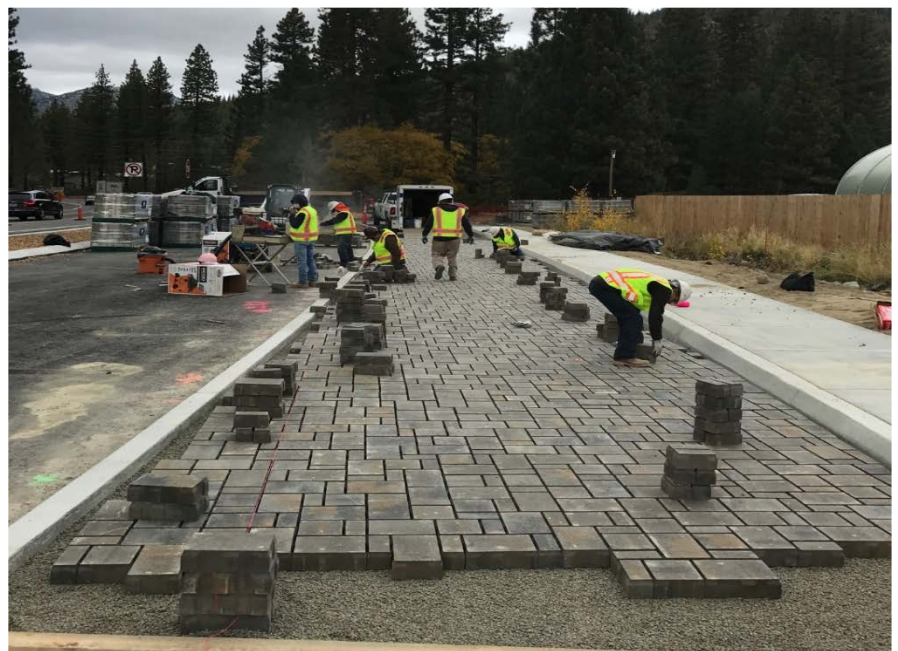

# GMP# 2 Construction – 2017 Construction



# Phase 2 Construction – 2018 Construction

