



**NDOT CWG Meeting
Update**
Sept 10, 2018



Cost

\$57,860,610

60% Spent to Date (\$35M)

Schedule

82% Complete (392/478 calendar days)

100% Design Complete

55% Construction Complete

NOTICE TO PROCEED

1. Aug 15, 2017
2. Nov. 13, 2017


CONSTRUCTION START

Jan./Feb. 2018

SUBSTANTIAL COMPLETION

End of 2018


Cost and Schedule

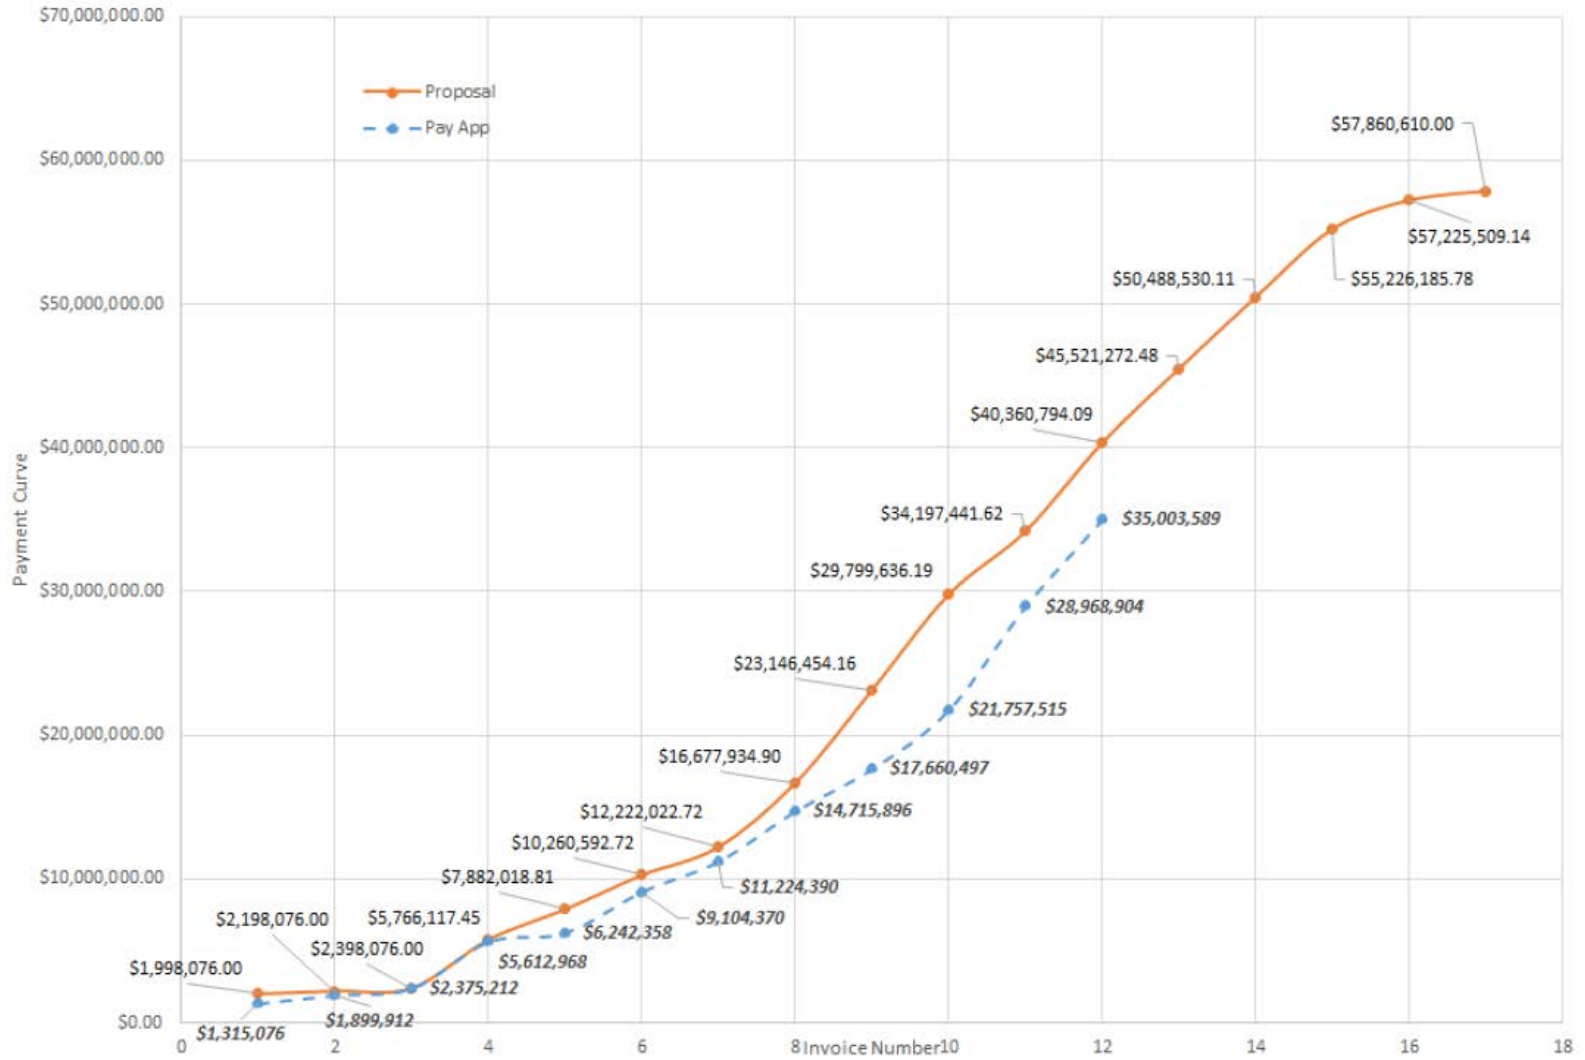

- I-15 phase 1 bridge complete
 - I-15 phase 2 bridge demo and construction began 9/4
- Grand Valley Parkway Bridge
 - Set Girder 9/5
- US-93 traffic shifted to new northbound alignment
 - US-93 southbound alignment and frontage road under construction
- Storm Drain structures under construction
- Modified Diverging Diamond partial completion

Change Orders

| Change Order | Description | Cost | Status | Initiated |
|--------------|---|-----------------------|----------------------|-----------|
| 01 | Frontage Road Extension | \$912,957.00 | Executed | NDOT |
| 02 | FRCL07 Re-route | \$320,490.72 | Executed | NDOT |
| 03 | VECP Culvert Elimination | (\$181,216.22) | Executed | Ames |
| 04 | Construction Traffic Control Measures for US-93 | \$69,180.00 | Executed | NDOT |
| 05 | CNLV Culvert Additions | \$4,150,004.00 | Pricing negotiations | CNLV |
| 06 | US93 SB Left Turn & additional conduits | \$241,243.35 | Executed | NDOT |
| | Totals | \$5,512,659.24 | | |

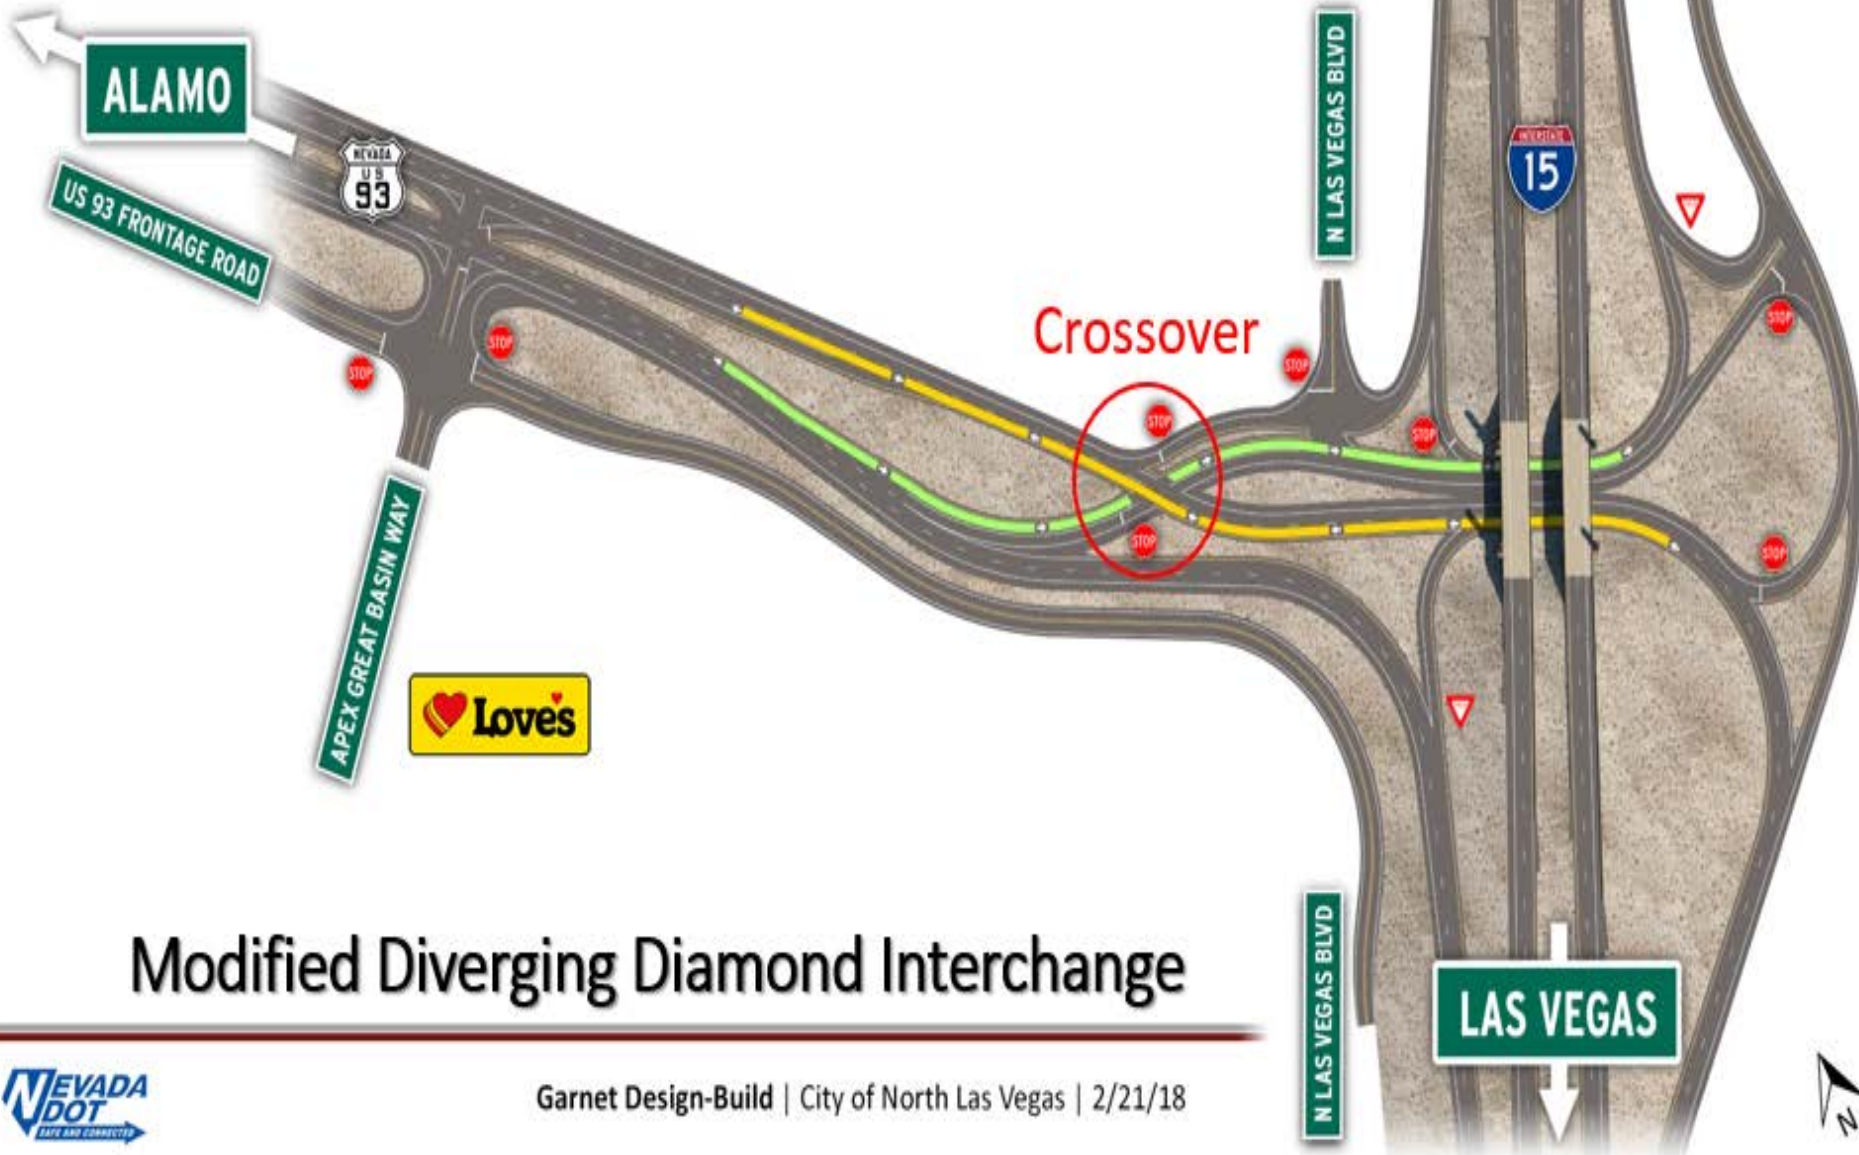

Modified Diverging Diamond Interchange
